


# Madera South High School: Football Scoreboard Replacement: Bid No. 102124

## Pre-Bid RFI Log

Question		Response
1	Is the contractor responsible for demo of the existing scoreboard? If so, please specify extents/scope.	Yes, the contractor is responsible for the removal of the existing scoreboard. The contractor is also responsible to make sure that the soils are recompacted sufficiently to meet installation specs for the new scoreboard. Any concrete demolition should be taken to nearest expansion joint.
2	Please provide geotechnical report for determination of existing soil conditions and cohesion.	No Geotech report was needed due to scope of project and code minimums were used in DSA approved PC plans.
3	Sheet SP-1 detail 10 shows 3' between the scoreboard and the video display, is this for speaker installation? If so, who is installing them?	Yes, this area is for future speakers which are owner furnished, owner installed.
	Are we to provide HSS steel supports under this contract?	Contractor is responsible for supplying and installing the lateral boards and attachment shown in detail K on sheet SB5.2 as part of this contract.
4	Sheet SB0.1 Table A shows an add board (ADO-24-3), is this supposed to be installed in the 3' space between the scoreboard and video display, if so, who's installing?	This is owner furnished owner installed.
5	The engineers estimate seems low if the contractor is installing the scoreboard and video display board. Please confirm that installation of Owner furnished scoreboard and video display board is part of this contract.	No, owner furnished scoreboard and video display are owner furnished and owner installed.
6	Sheet SB5.1 details G & E shows solar panel and dome bracing installation, are these required?	No solar panel(s) or dome
7	Sheet SB.2 "Three Column Assembly" schedule requires heavier columns if flags are installed. Are flags being installed? If so, who's providing and installing?	No flags
8	Sheet SB5.3 detail C shows installation of aluminum truss. This would exceed the 23'-6" max height shown on sheet SP-1 detail 10. Is installation of the truss in this contract?	No truss
9	Will demo or installation of site concrete be required, if so, please provide details, grades, and extents.	Yes, concrete demolition will be required to remove the existing scoreboard and to establish pathway to nearest in-ground power and signal boxes. Any concrete demolition should be taken to nearest expansion joint.
10	Please provide accessible route for heavy equipment and site access.	See attached image.
11	Is the scoreboard being installed by the manufacturer?	Yes, the scoreboard is owner furnished and owner installed.
12	Is the truss option being utilized for this project?	No truss
13	Will the lateral board attachment on sheet SB5.2, detail K be installed by contractor or scoreboard manufacturer?	Contractor is responsible for supplying and installing the lateral board attachment shown in detail K on sheet SB5.2 as part of this contract.
14	Will the solar panel, speaker and video board attachment on page SB5.1. detail G, K, F, and J be utilized in this project? If so, provided and installed by whom?	No solar panel(s); no speakers; yes to the video board. Contractor shall supply brackets for video board(s) that are detailed in diagrams J and K on sheet SB5.1. Video board installation shall be accomplished by owner/scoreboard manufacturer.

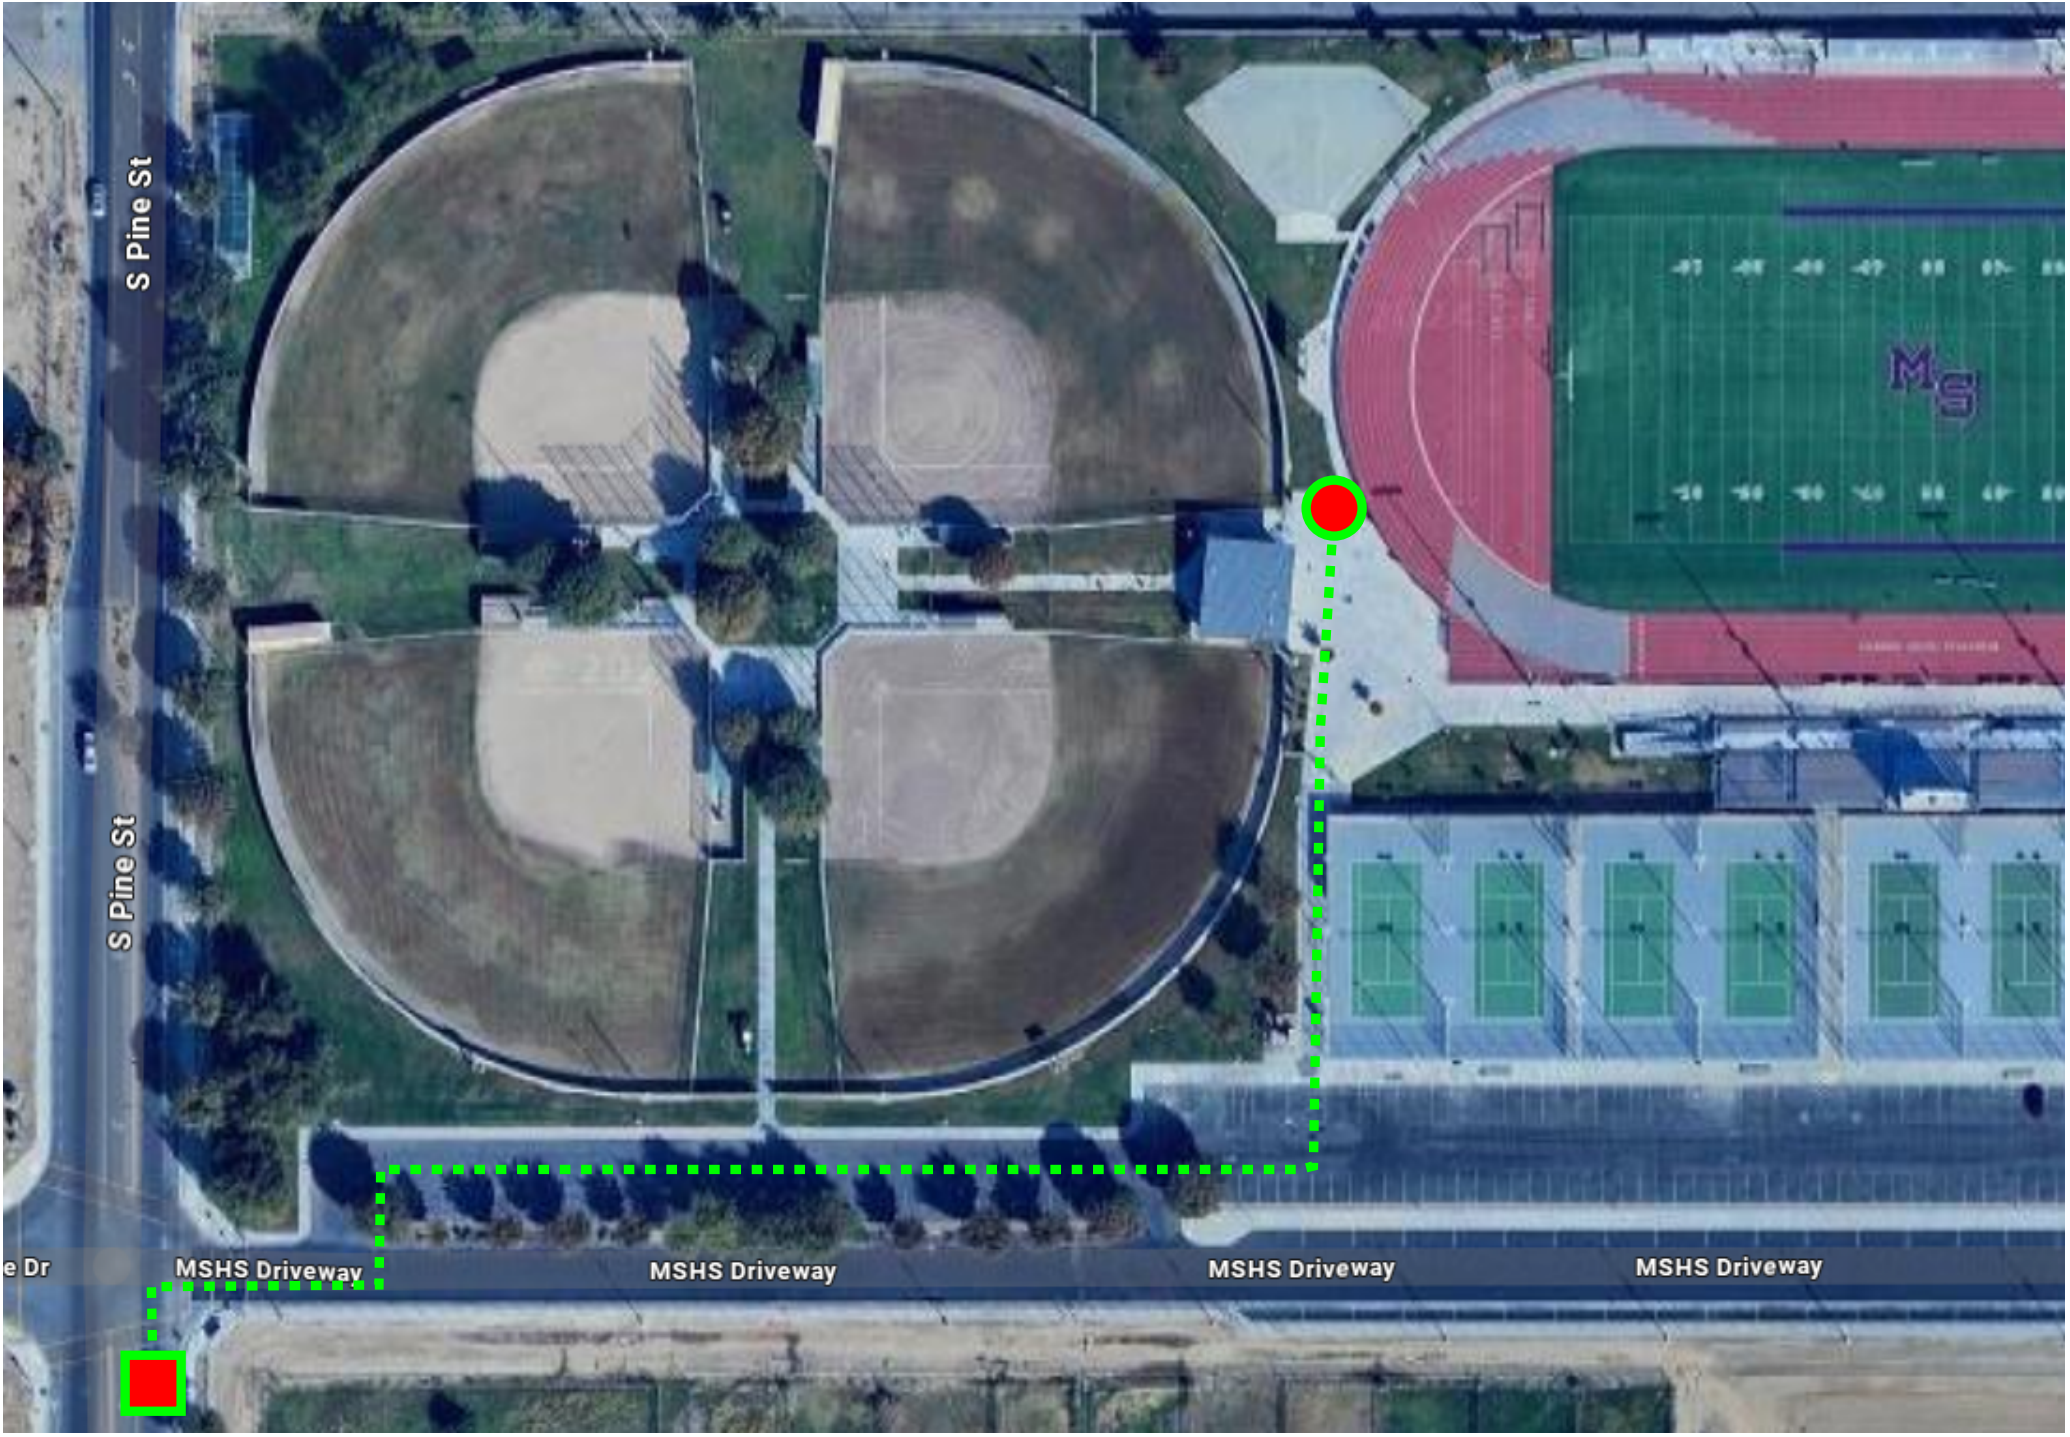

S Pine St

S Pine St

e Dr

MSHS Driveway

MSHS Driveway

MSHS Driveway

MSHS Driveway
